


KYL14284 - N Burleson St. Improvements - Construction

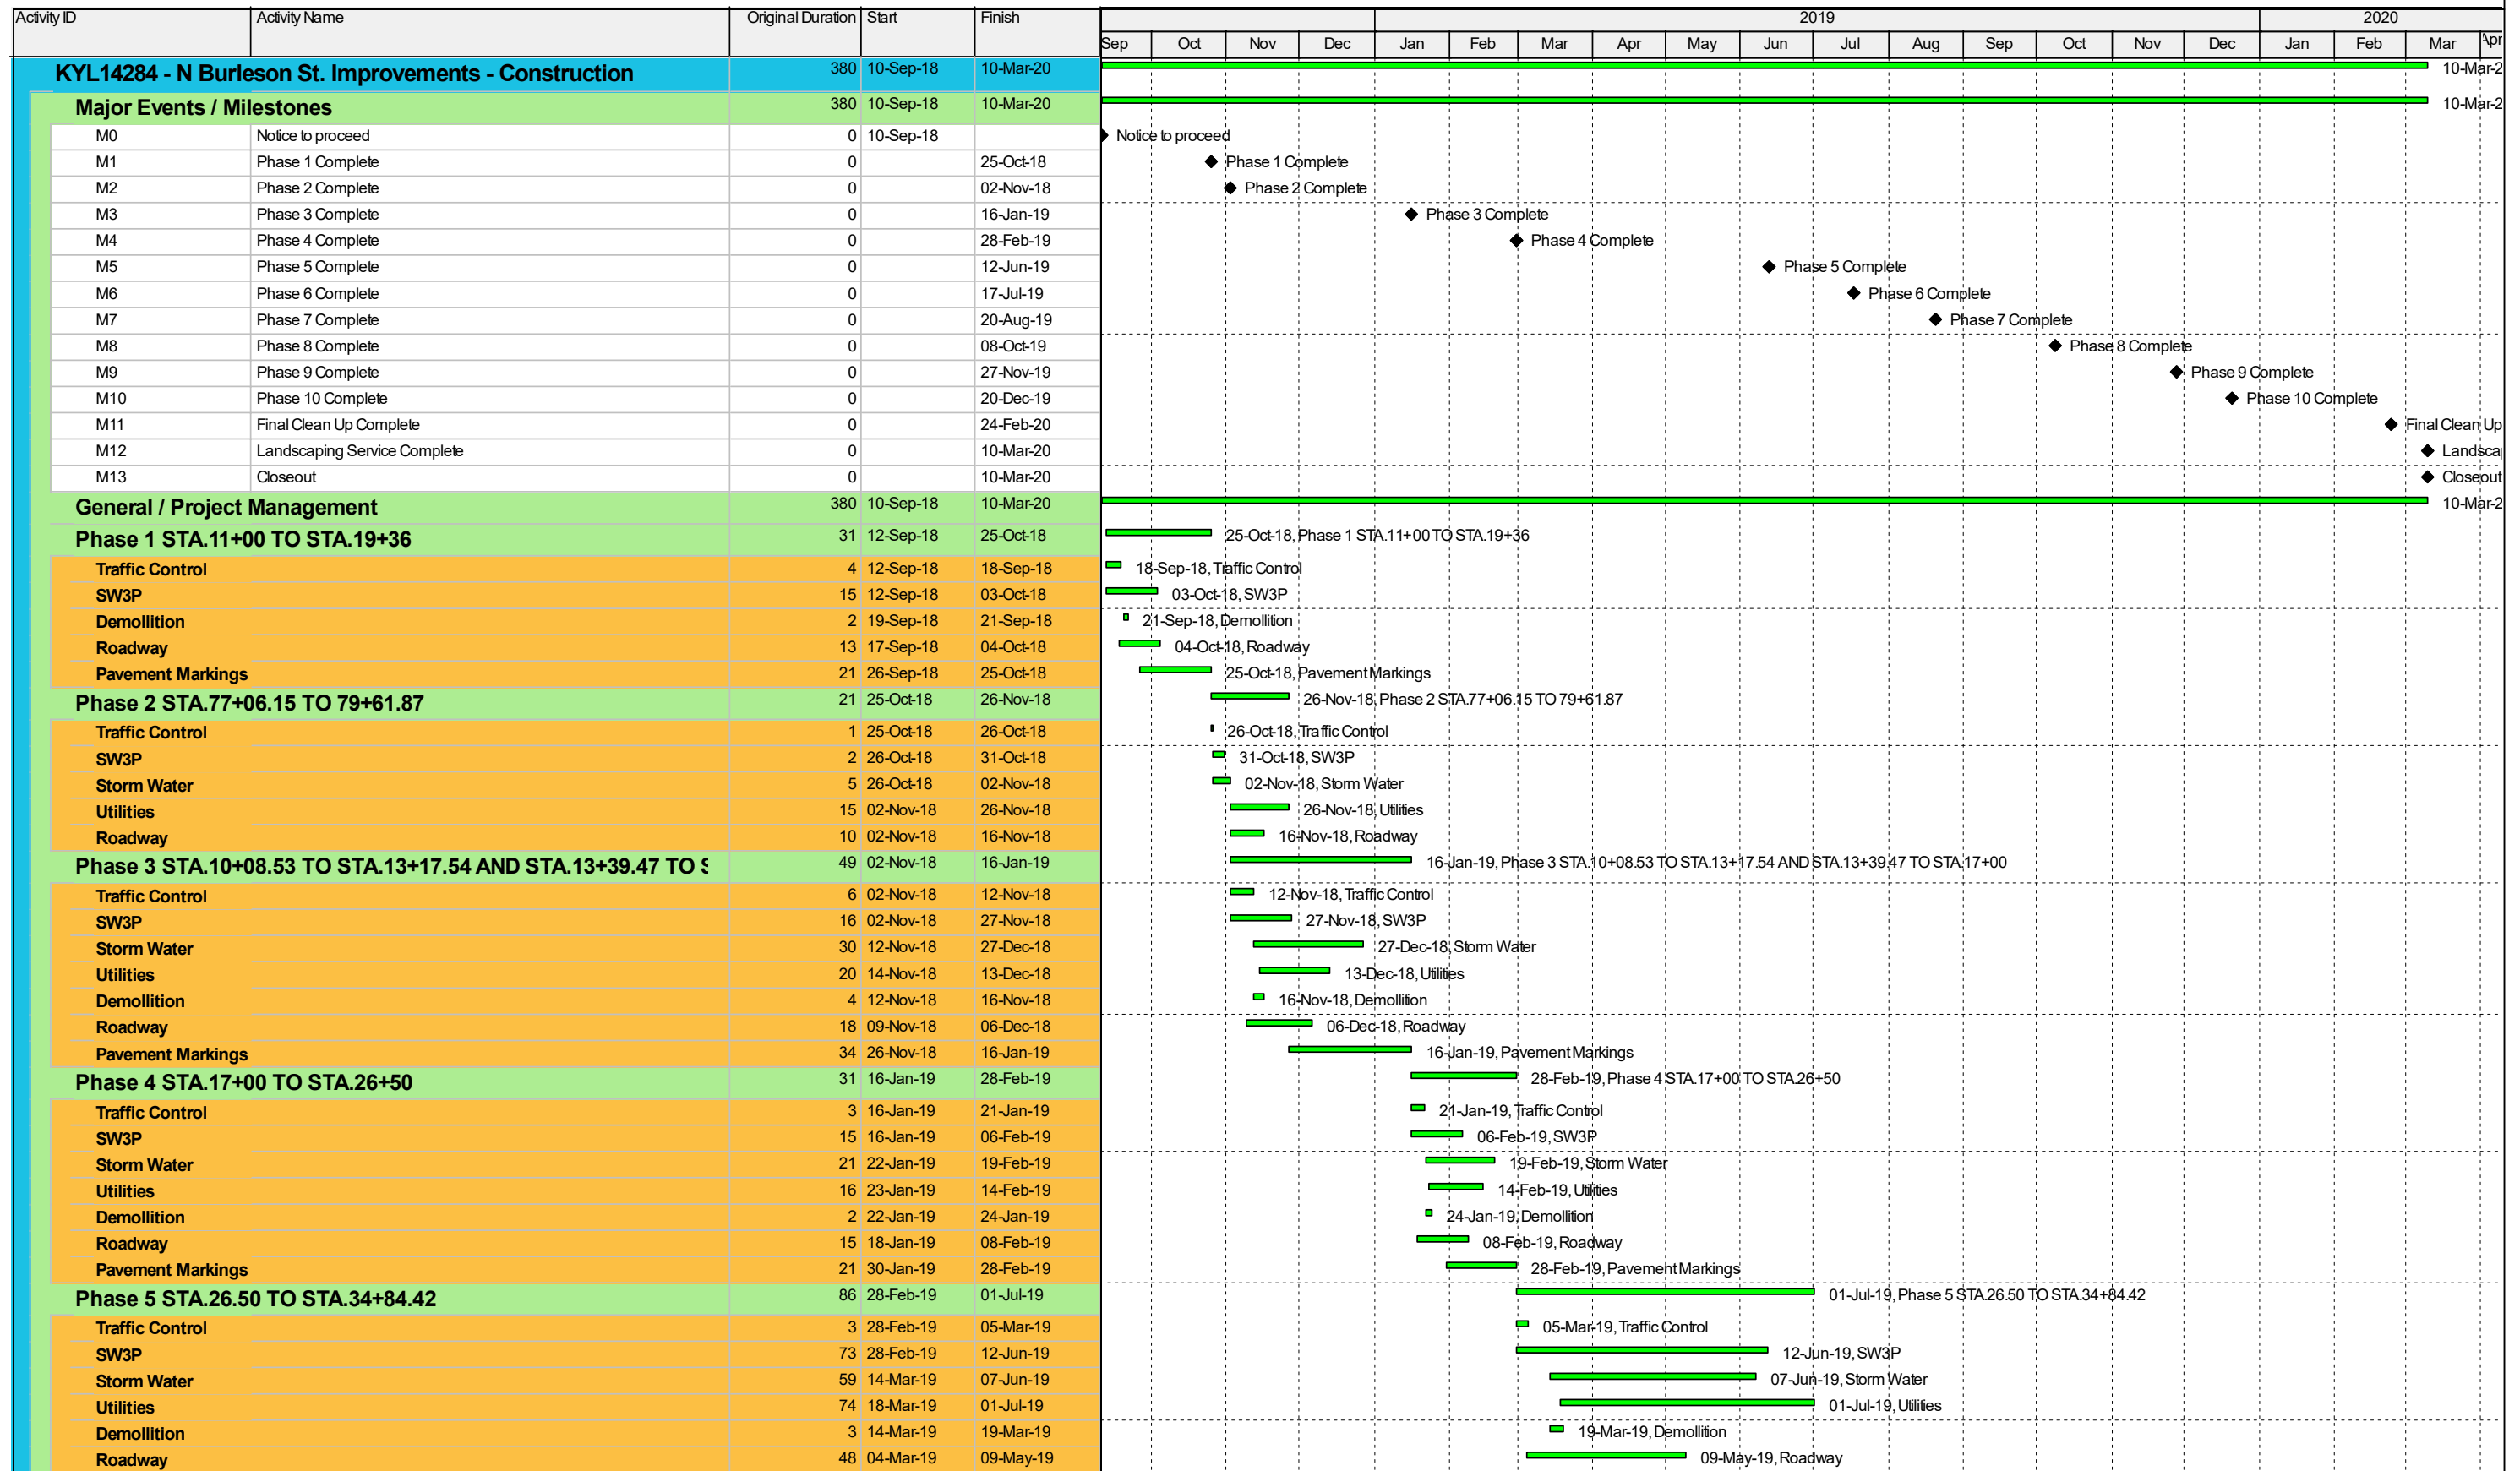

█ Remaining Level of Effort   
  Remaining Work   
 ▬ Summary  
 Actual Work   
 ◆ Milestone

**KYL14284 - N Burleson St. Improvements - Construction**

Activity ID	Activity Name	Original Duration	Start	Finish	2019												2020								
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
	<b>Pavement Markings</b>	48	04-Apr-19	12-Jun-19																					
	<b>Phase 6 STA.36+50 TO STA.38+00</b>	24	12-Jun-19	17-Jul-19																					
	Traffic Control	3	12-Jun-19	17-Jun-19																					
	SW3P	7	12-Jun-19	21-Jun-19																					
	Storm Water	15	17-Jun-19	09-Jul-19																					
	Utilities	8	18-Jun-19	28-Jun-19																					
	Demolition	2	17-Jun-19	19-Jun-19																					
	Roadway	9	14-Jun-19	27-Jun-19																					
	Pavement Markings	16	24-Jun-19	17-Jul-19																					
	<b>Phase 7 STA.34+84.42 TO 36+50</b>	24	17-Jul-19	20-Aug-19																					
	Traffic Control	3	17-Jul-19	22-Jul-19																					
	SW3P	7	17-Jul-19	25-Jul-19																					
	Storm Water	15	22-Jul-19	12-Aug-19																					
	Utilities	8	23-Jul-19	02-Aug-19																					
	Demolition	2	22-Jul-19	24-Jul-19																					
	Roadway	9	19-Jul-19	01-Aug-19																					
	Pavement Markings	16	29-Jul-19	20-Aug-19																					
	<b>Phase 8 STA.36+50 TO STA.52+00</b>	47	20-Aug-19	25-Oct-19																					
	Traffic Control	3	20-Aug-19	23-Aug-19																					
	SW3P	22	20-Aug-19	20-Sep-19																					
	Storm Water	42	26-Aug-19	25-Oct-19																					
	Utilities	39	27-Aug-19	22-Oct-19																					
	Demolition	2	26-Aug-19	29-Aug-19																					
	Roadway	16	22-Aug-19	16-Sep-19																					
	Pavement Markings	25	03-Sep-19	08-Oct-19																					
	<b>Phase 9 STA.52+00 TO STA.61+85</b>	36	08-Oct-19	27-Nov-19																					
	Traffic Control	3	08-Oct-19	11-Oct-19																					
	SW3P	22	08-Oct-19	07-Nov-19																					
	Storm Water	23	15-Oct-19	14-Nov-19																					
	Utilities	24	15-Oct-19	18-Nov-19																					
	Demolition	2	15-Oct-19	17-Oct-19																					
	Roadway	17	10-Oct-19	04-Nov-19																					
	Pavement Markings	26	22-Oct-19	27-Nov-19																					
	<b>Phase 10 STA.66+97.21 TO STA.77+06.15</b>	16	27-Nov-19	20-Dec-19																					
	Traffic Control	1	27-Nov-19	29-Nov-19																					
	SW3P	2	29-Nov-19	04-Dec-19																					
	Roadway	12	04-Dec-19	20-Dec-19																					
	<b>Illumination</b>	43	04-Nov-19	08-Jan-20																					
	Illumination	43	04-Nov-19	08-Jan-20																					
	<b>Landscaping</b>	45	07-Jan-20	10-Mar-20																					
	Landscaping	31	07-Jan-20	19-Feb-20																					
	Landscaping Service	30	28-Jan-20	10-Mar-20																					
	<b>Final Clean Up</b>	19	28-Jan-20	24-Feb-20																					
	Final Clean Up	19	28-Jan-20	24-Feb-20																					
	<b>Closeout</b>	30	28-Jan-20	10-Mar-20																					

Remaining Level of Effort 
  Remaining Work 
  Actual Work

Milestone
