



# CIP/Road Projects Update

February 18, 2020

Leon Barba, P.E.

Engineering Department



## Lehman Road

- Based on pay estimates, overall project is 48% complete
- Paved from Primrose to FM 150 and open to local traffic only
- Bridge at Plum Creek 20% complete with an estimated completion in April
- Overall project expected completion August 2020







# Burleson Street

- Based on pay estimates, overall project is 74% complete
- Section from Center to Rodriguez is open to local traffic only with workers in the section
- North of Rodriguez to south of roundabout closed





## Burleson Street (cont.)

- Burleson north of roundabout open to local traffic only
- Utility crew working north of roundabout
- UPRR re-planking is complete
- Estimated completion June 2020








# Bunton Creek Interceptor


- Based on pay estimates, overall project is 98% complete
- Preparing for final walk-through
- Working on punchlist items
- 100% completion by 03/31/2020

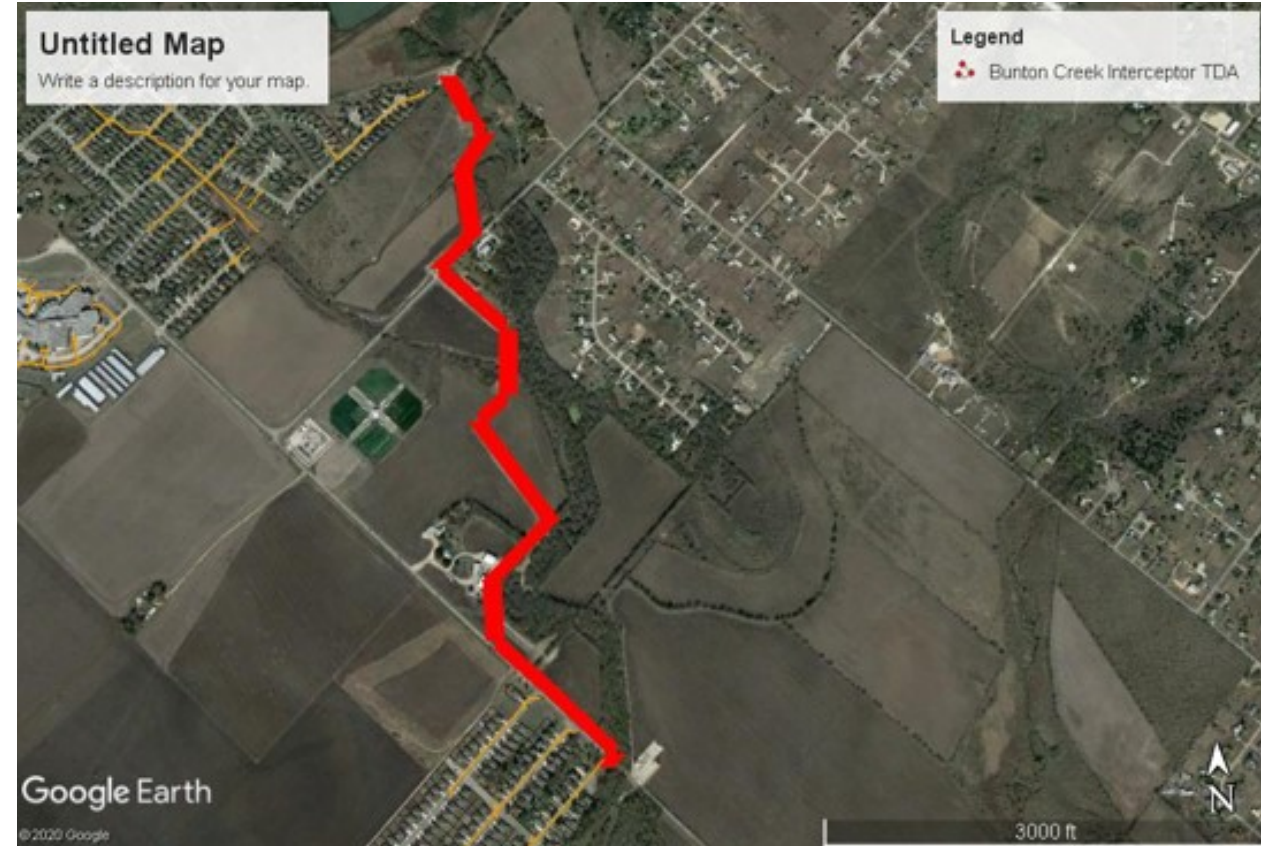



# WWTP Expansion

- Bid Award February 4, 2020
  - Funding approved \$30,338,070 w/5% contingency
  - Contractor: Archer Western, LLC
  - Contract documents being prepared for signature by all parties end of February
  - Tentative construction to begin late March
- 650 Days to Construct

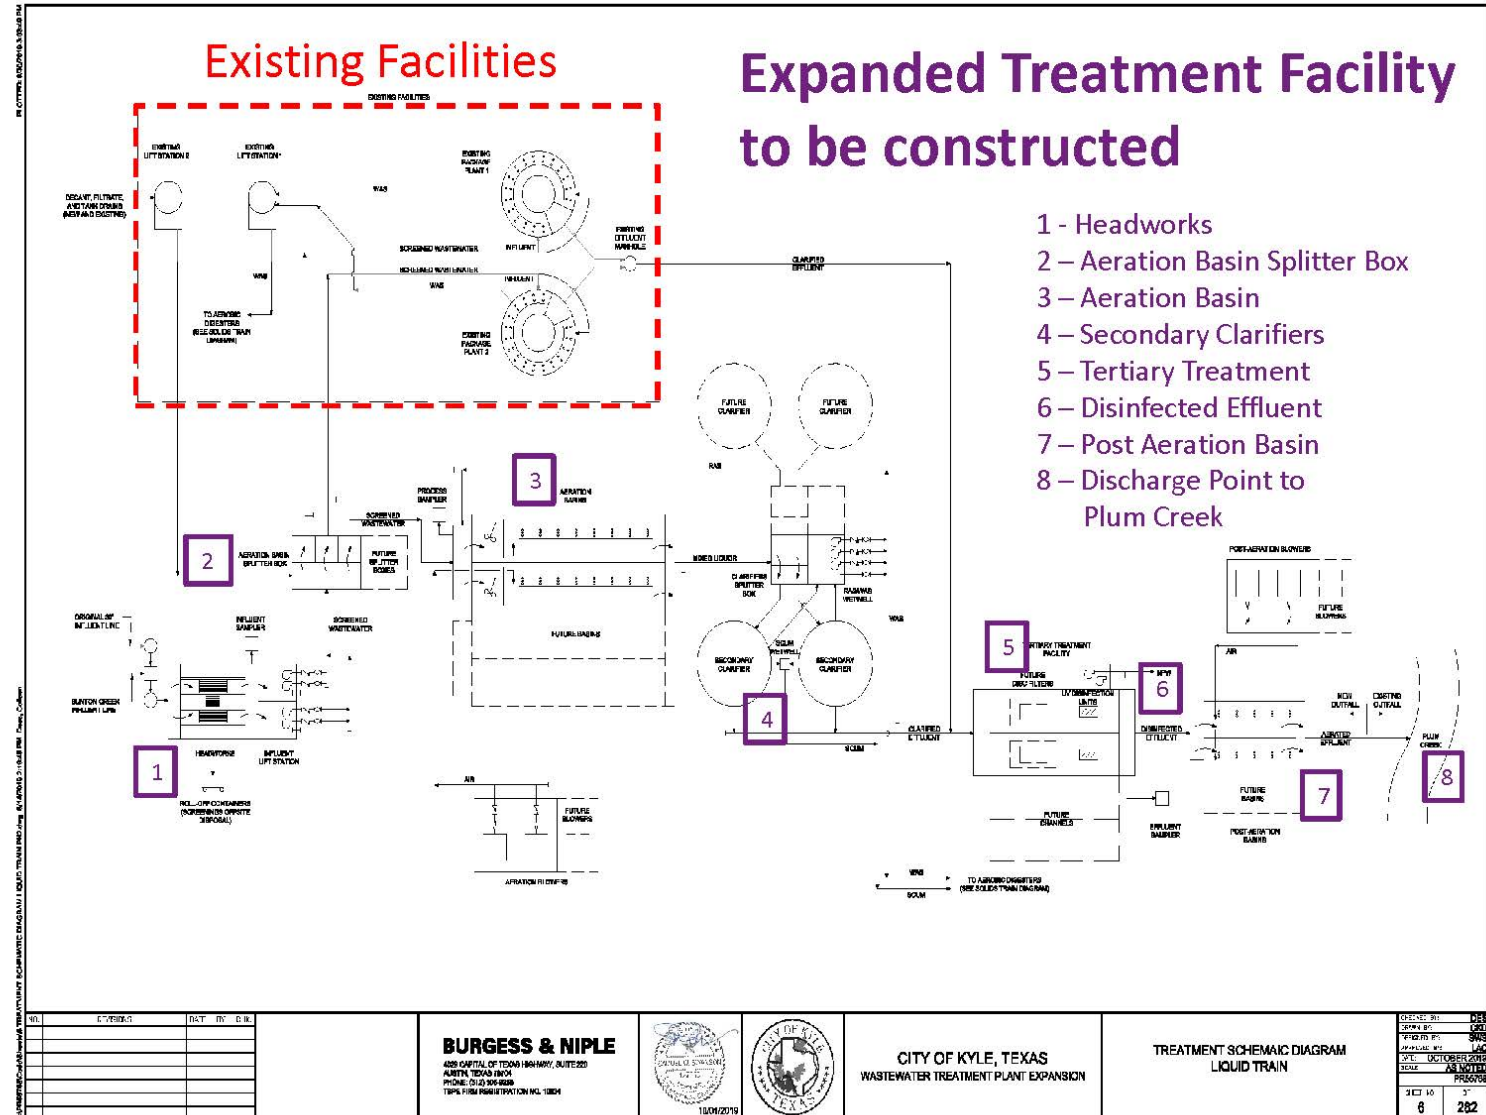



# Other Projects/Consent Agenda

## Plum Creek Wastewater Interceptor Phase 1 Improvements (Springbranch)

- Final walk-through completed
- Finalizing punchlist items

## Well #4 Elevated Storage Tank

- Consent Agenda Item #13

## Schlemmer & Porter St. WW Project

- Consent Agenda Item #14

