



CIP/Road Projects Update

March 3, 2020

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 53% complete
- Bridge at Plum Creek 40% complete with an estimated completion in April
- Day closure(s) planned March 16th-20th from FM 150 to Masonwood
- Overall project expected completion August 2020





Burleson Street

- Based on pay estimates, overall project is 74% complete
- Section from Center to Rodriguez is open to local traffic only with workers in the section
- Pavement distresses occurring at Schlemmer and Live Oak; groundwater encountered
- North of Rodriguez to south of roundabout closed





Burleson Street (cont.)

- Burleson north of roundabout open to local traffic only
- Utility crew working north of roundabout; 50% complete
- UPRR work is complete
- Estimated completion June 2020





Southside Wastewater Improvements Project


- Consent Agenda Item #11
 - Additional engineering services
- Consent Agenda Item #12
 - Acquiring easements
- Based on pay estimates, overall project is 45% complete





WWTP Expansion

- Consent Agenda Item #10
 - Burgess & Niple Construction Phase Services
- Funding approved \$30,338,070 w/5% contingency
- Contractor: Archer Western, LLC
 - Contract documents executed February 26, 2020
 - Notice to proceed April 13, 2020
- 650 Days to Construct

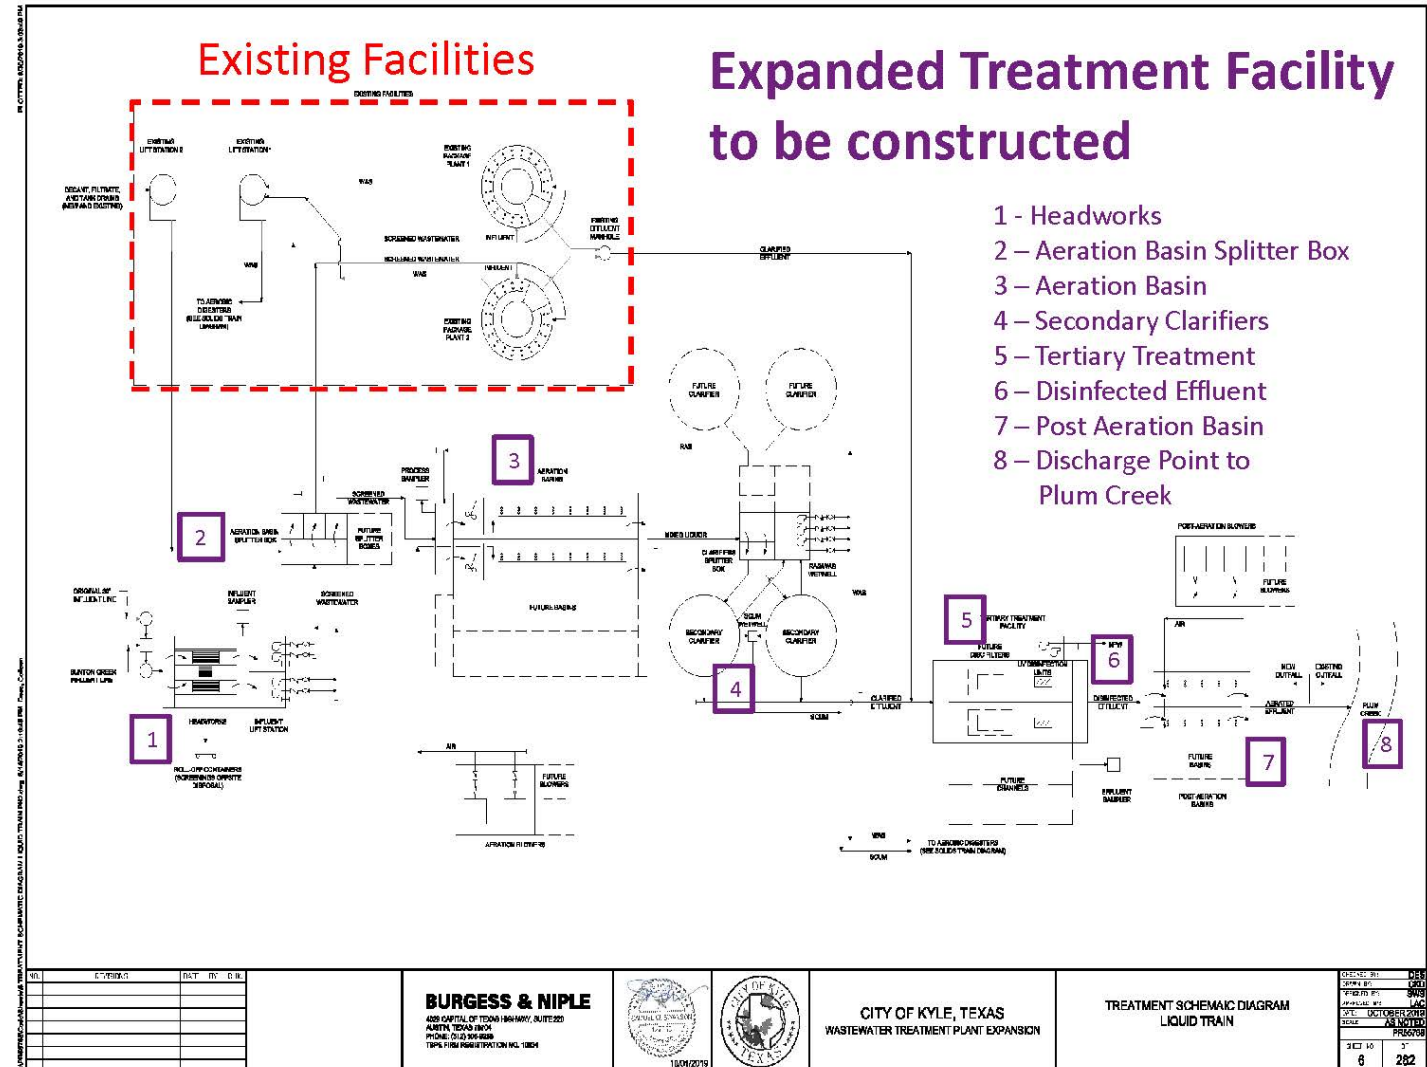



Substantially Completed Projects

Plum Creek Wastewater Interceptor Phase 1 Improvements (Springbranch)

- Final walk-through completed
- Finalizing punchlist items

Bunton Creek Interceptor

- Completing as-built survey on manholes
- Final walk-through this month
- 100% completion by 03/31/2020

