



CIP/Road Projects Update

June 2, 2020

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 67% complete
- Bridge at Plum Creek complete
- Lehman closed from Hiver to Bunton Creek Rd
- Overall project expected completion August 2020





Burleson Street

- Based on pay estimates, overall project is 83% complete
- Pavement distresses occurring from Lockhart to Live Oak due to groundwater
- French drain construction underway
- Utilities north of roundabout; 95% complete
- Estimated substantial completion August 2020





Southside Wastewater Improvements Project

- Consent Agenda Item No. 19 for additional negotiations to acquire remaining easements
- Based on pay estimates, overall project is 52% complete
- One crew working on the Post Road lift station
- Second crew working on gravity line near Public Works






WWTP Expansion

- Consent Agenda Item No. 11 for 20' utility easement for temporary electrical service to construction trailer
- Notice to proceed issued May 26, 2020
- Construction Trailer on site, powered w/generator
- Public at property line taking photos
- Contractor concerned about drones and existing power lines



Contractor Entrance Signage

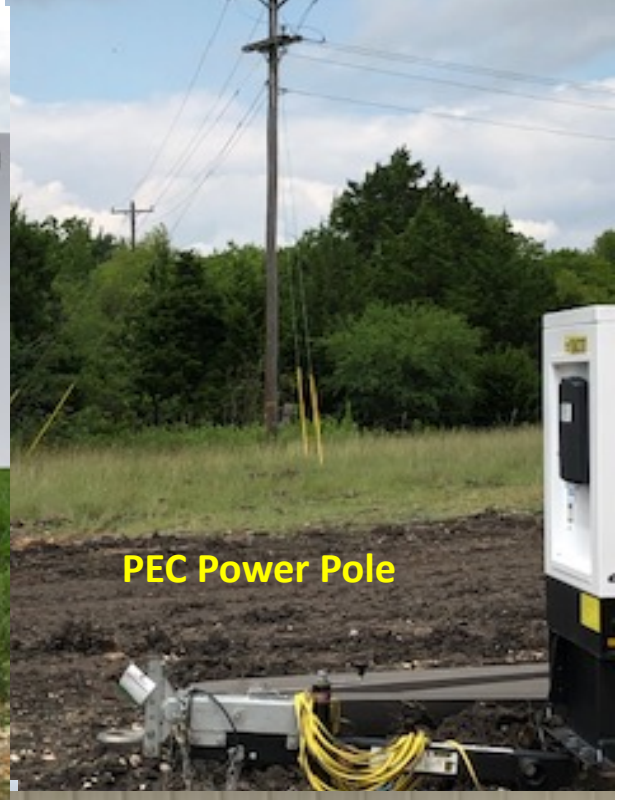

PEC Power Pole



Contractor Trailer On Site



Contractor Required Documents Postings



Other Projects/Consent Agenda

Indian Paintbrush Lift Station Force Main Relocation

- Consent Agenda Item No. 13
 - Hays County dedicated easement for relocation of a wastewater force main required by the Dacy Lane Road Improvements

FM 1626 Pump Station Improvements

- Consent Agenda Item No. 17
 - Preliminary Engineering Report for the proposed FM 1626 Pump Station Improvements
