



# CIP/Road Projects Update

June 16, 2020

Leon Barba, P.E.

Engineering Department



## Lehman Road

- Based on pay estimates, overall project is 74% complete
- Bridge at Plum Creek complete
- Lehman closed from Hiver to Bunton Creek Rd
- Overall project expected completion August 2020








## Burleson Street

- Based on pay estimates, overall project is 83% complete
- French drain construction underway to address groundwater (60% complete)
- Utilities north of roundabout complete
- Bore for water utility starting next week, weather permitting
- Estimated substantial completion August 2020

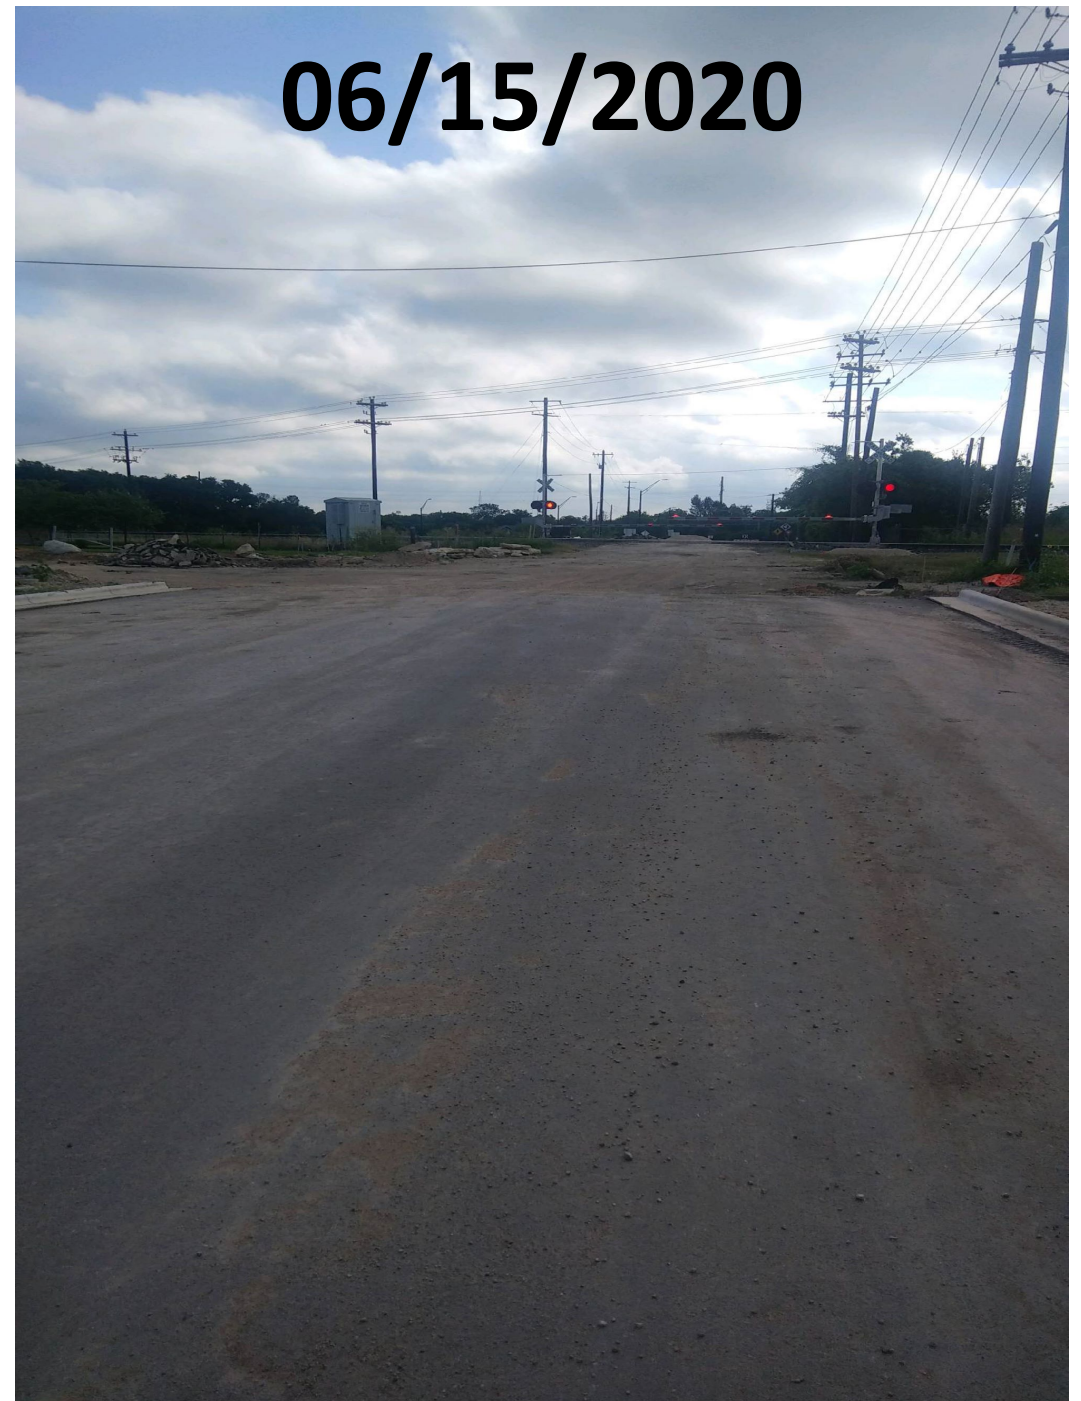





# Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 52% complete
- One crew working on the Post Road lift station
- Second crew working on gravity and reclaimed water lines near Public Works







# WWTP Expansion

- Notice to proceed issued May 26<sup>th</sup>
  - 650 days to substantial completion
- Excavation of headworks underway
- Construction Manager/Construction Inspector contract scheduled for July 7<sup>th</sup> council meeting

## WWTP Construction Schedule

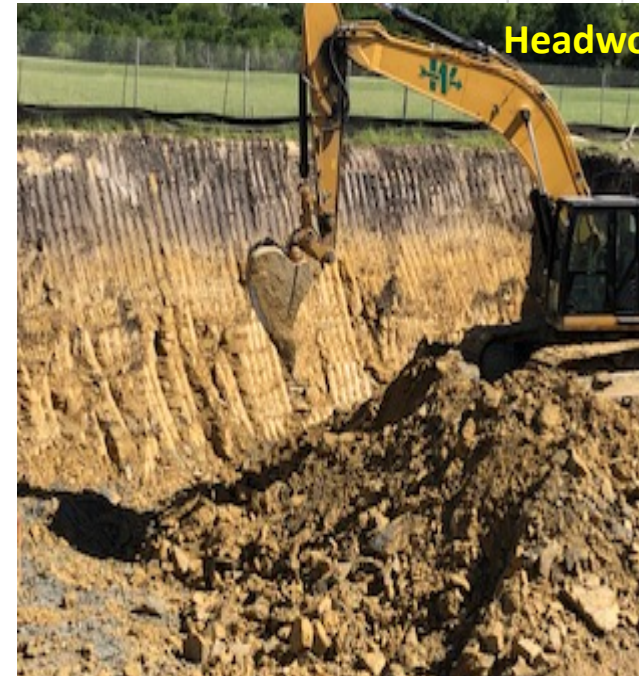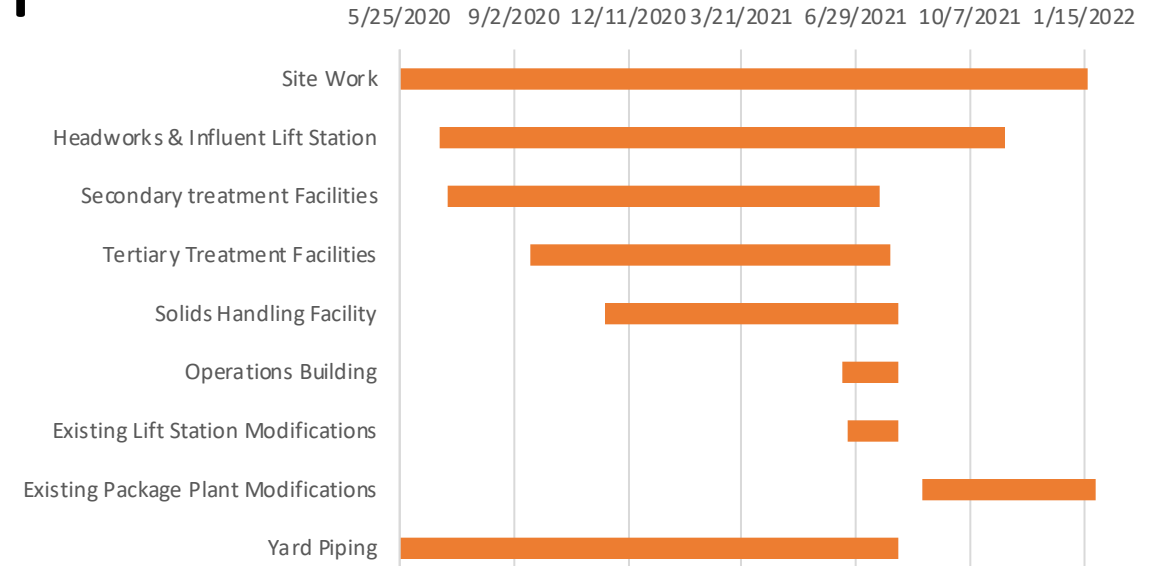

Headworks Excavation

