



CIP/Road Projects Update

November 4, 2020

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 98% complete
- Contractor working on final walk-through items
- ADA repairs in progress
- Bridge seal this week





Burleson Street

- Based on pay estimates, overall project is 93% complete
- Items on punch list being addressed by contractor
- Finalization of work quantities in progress





Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 69% complete
- One crew working on the Post Road lift station
- Second crew working on gravity and reclaimed water lines near TDCJ
- Third crew working on bores on north end of project





WWTP Expansion Project

- Based on pay estimates, overall project is 14.41% complete. November pay application under review
- Form work, rebar and pipe installation at all major treatment units ongoing
- Continued installation of electrical duct banks and manholes throughout site
- No deviations between construction progress and construction schedule



UV
Disinfection

Type 1 Floodwall Berm

Aerobic
Digesters

Plant #1

Clarifiers

Headworks/Influent
Lift Station

Plant #2

Aeration Basins

Aeration
Splitter Box

WWTP
EXPANSION
OCTOBER 30,
2020

Electrical Duct Bank

Operations
Building

Headworks/Influent Lift Station





Bunton Creek Interceptor Ph 2

- Bunton Creek Village Lift Station to COK Wastewater Treatment Plant
- Preconstruction meeting scheduled for next week
- 250 calendar day contract
- Start Work Date: December 1, 2020



Well Site #4 Elevated Storage Tank Rehabilitation

- 150 calendar days for full completion
- Start date: December 15, 2020





Elliott Branch Wastewater Improvements Phase 1

- Scheduled for Council approval on November 17, 2020



Old Post Road


- Meeting scheduled with Hays County on November 18, 2020 to continue project coordination
- TxDOT permitting underway
- Negotiations continuing for ROW
- Hays County reviewing draft interlocal agreement



Developer Project

Casetta Ranch Roundabout

- Construction of a roundabout at Bunton Lane & Goforth
- Construction to start November 4, 2020
- Estimated duration 3 months

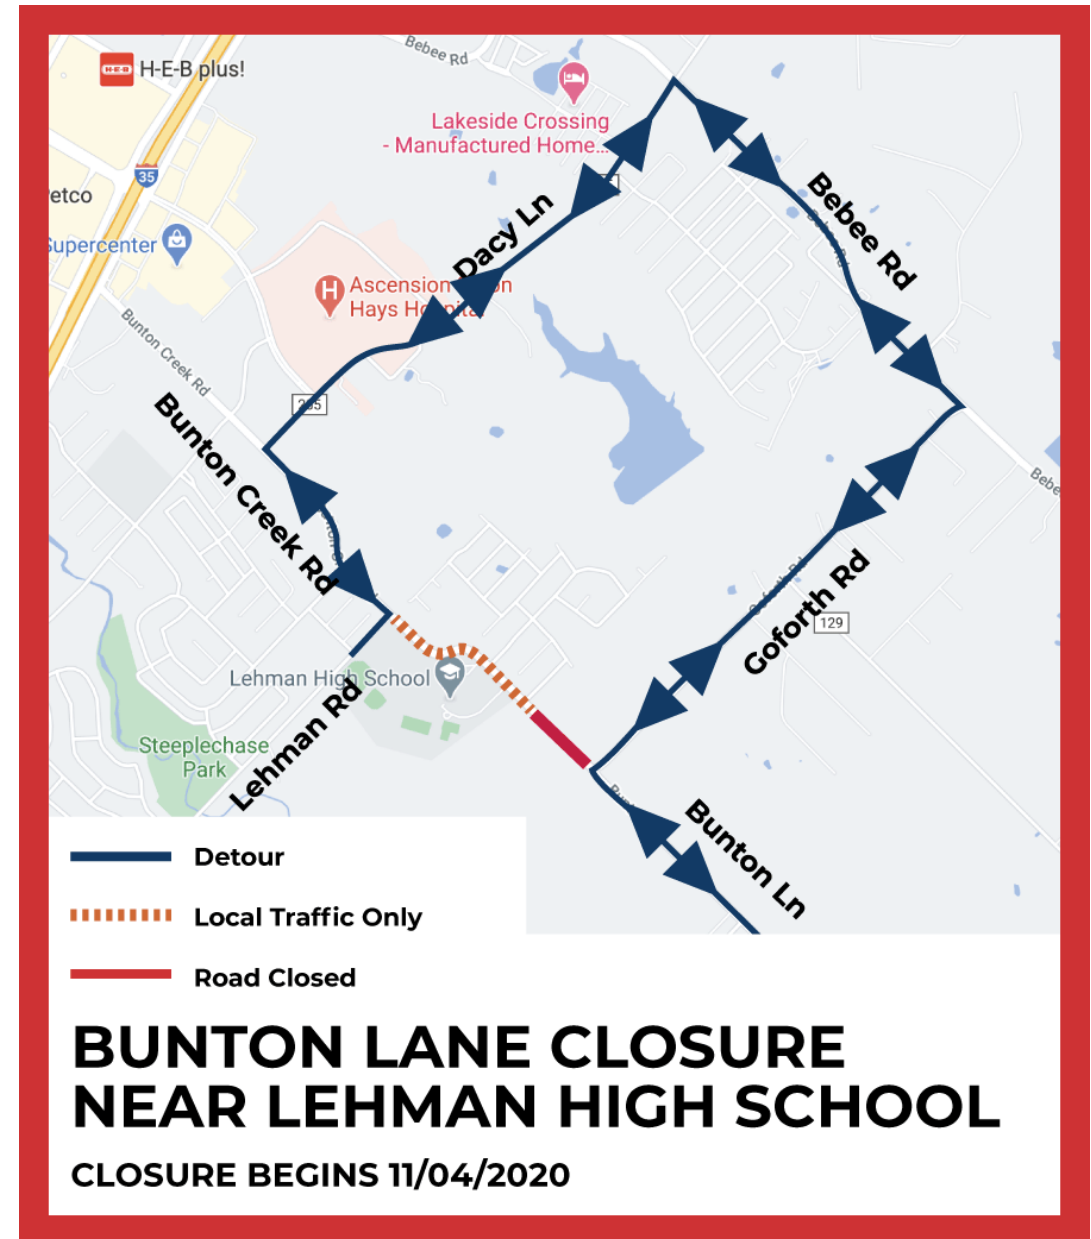



Consent Agenda Item

Temporary Reduction in Speed Limit on NB Frontage Road of IH-35

- Consent Agenda Item No. 17
- TxDOT Project
- Temporary speed limit reduction from 55 mph to 45mph
