



CIP/Road Projects Update

November 19, 2019

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 42% complete
- Paving from Primrose to FM 150 today; road will remain closed for sidewalk & driveway crews
- **Tentative** opening of that section could be as early as mid-December
- Overall project expected completion August 2020





Burleson Street

- Based on pay estimates, overall project is 66% complete
- Section from Center to Live Oak is open to local traffic only
- Work continues on the retaining wall at the church
- Detention pond nearing completion
- Crews working from Live Oak to S. of James Adkins





Burleson Street (cont.)

- New traffic routing started Wednesday, October 23rd with Rodriguez and Spring Branch closed
- Utility work continues from Rodriguez to James Adkins
- UPRR track closure will coincide with the city's closure from James Adkins to the Roundabout tentatively scheduled the week of December 9, 2019
- During the closure north of James Adkins, traffic will be allowed to use Burleson up to Star of Texas; however, workers will be present finishing detailed work
- Estimated completion June 2020



Kyle Crossing

- Project 75% complete
- Estimated completion December 2019 per contract



11/19/2019



Bunton Creek Interceptor


- Overall Project is 96% complete
 - Working on punch list items
- Preparing for final walk-through
- 40% of Project is grant funded





WWTP Expansion

- New Project Manager for the City – Yvonne Gil-Vallejo
- Bid opening scheduled for December 3, 2019
- Scheduled for Council review/approval on December 17, 2019

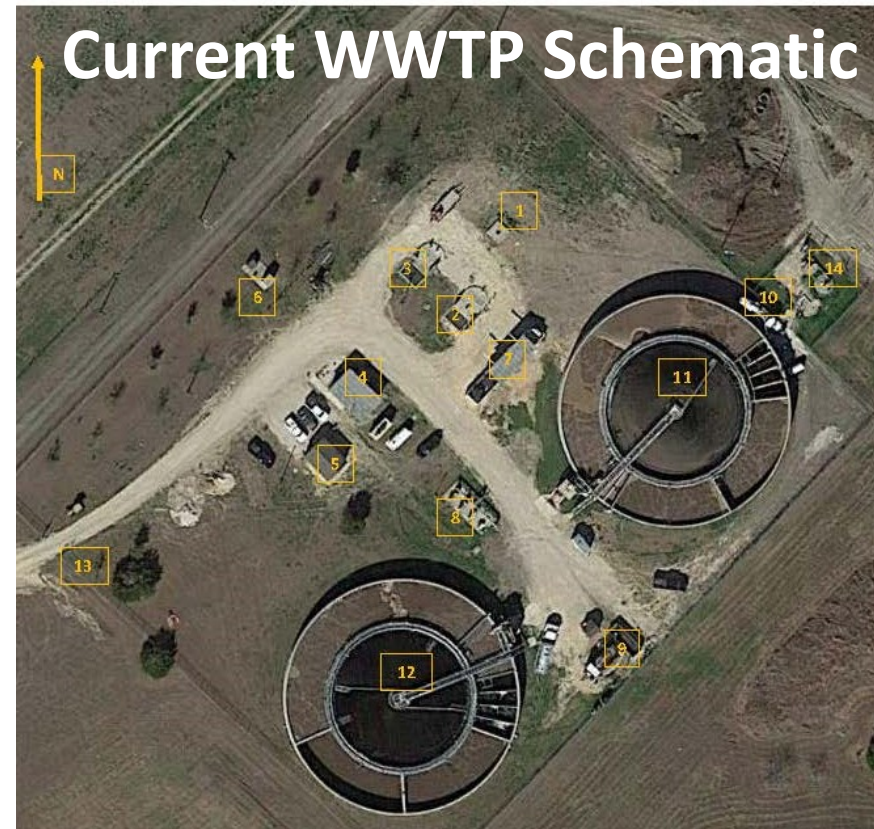

- | | |
|-----|---|
| 1. | Main Manhole |
| 2. | Liftstation 1 |
| 3. | Liftstation 2 |
| 4. | Motor Control |
| 5. | Office |
| 6. | Primary Electrical Feed |
| 7. | Chemical Control |
| 8. | Blowers |
| 9. | Sludge Handling |
| 10. | Plant Reclaimed Water System |
| 11. | Treatment Train 1 |
| 12. | Treatment Train 2 |
| 13. | Main access |
| 14. | Plum Creek Golf course Effluent Station |



Other Projects

Plum Creek Wastewater Interceptor Phase 1 Improvements (Springbranch)

- Overall project is 87% complete

Marketplace Ave Extension

- Safety lighting should be in-place by the end of November; delay due to installation error
- PEC will need to provide power
- City will provide inspections
- Operational in November

