



# CIP/Road Projects Update

December 1, 2020

Leon Barba, P.E.

Engineering Department



## **Lehman Road**

- Punch list items addressed 12/1/2020
- Project closeout in progress

## **Burleson Street**

- Based on pay estimates, overall project is 93% complete
- Items on punch list being addressed by contractor
- Finalization of work quantities in progress



# Windy Hill Street & Drainage Project

- Part of a 2015 Community Block Grant Disaster Recovery Program for communities impacted by the 2015 floods
- Authorized for Project Development
  - Oct 7, 2019 - November 15, 2021 (engineering, environmental, ROW, construction)
- Funded jointly by the General Land Office (\$1,847, 862.05) & City of Kyle participation (\$1,649,824.13)





# Windy Hill Street & Drainage Project (cont.)

- Construction began on November 30, 2020
- 1<sup>st</sup> Phase of project involves demolition & construction of the Richmond Branch structure as well as temporary pavement needed for the next phase of construction





# Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 71% complete
- One crew working on the Post Road lift station
- Second crew working on gravity and reclaimed water lines near TDCJ
- Third crew working on bores on north end of project






# WWTP Expansion Project

- Based on pay estimates, overall project is 20% complete. December pay application under review.
- Treatment pipe, form work, rebar and concrete placement continues on all major treatment units
- Continued installation of electrical duct banks and manholes throughout site
- No deviations between construction progress and construction schedule



# WWTP Expansion Project (cont.)

Headworks & Influent Lift Station

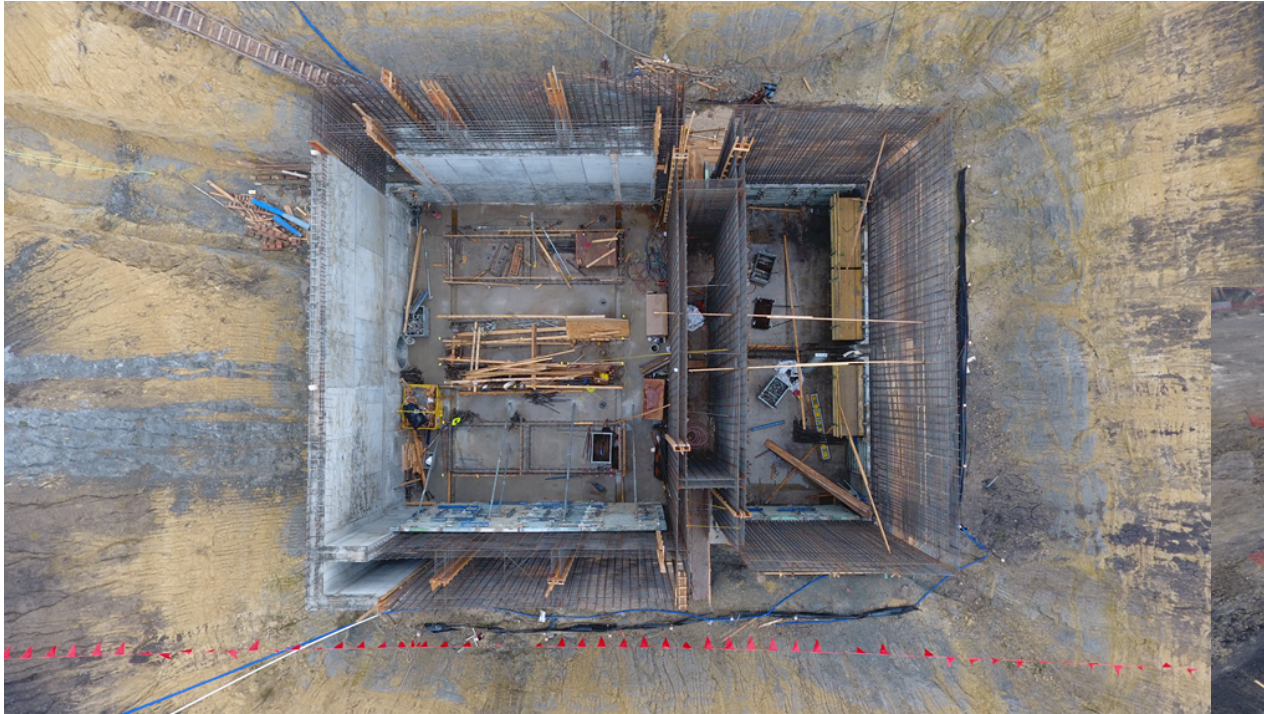

November 27, 2020

Clarifiers 1A & 1B





## Bunton Creek Interceptor Ph 2

- Bunton Creek Village Lift Station to COK Wastewater Treatment Plant
- 250 calendar day contract
- Start Work Date: December 7, 2020





# Well Site #4 Elevated Storage Tank Rehabilitation

- 150 calendar days for full completion
- Start date: December 15, 2020





## Old Post Road

- Next meeting scheduled with Hays County on December 16, 2020 to continue project coordination
- TxDOT permitting underway
- Negotiations continuing for ROW
- Hays County reviewing draft interlocal agreement



# Developer Project

## Casetta Ranch Roundabout

- Construction of a roundabout at Bunton Lane & Goforth
- Construction started November 4, 2020
- Estimated duration 3 months
- Approximately 40% complete





# Developer Project

## Paramount Subdivision

- Opal Lane – traffic control plan under review
- Construction on Opal Lane will begin within one week of the plan being approved



**For info & updates on all projects visit:**

**[cityofkyle.com/projects](http://cityofkyle.com/projects)**
