



CIP/Road Projects Update

December 15, 2020

Leon Barba, P.E.

Engineering Department



Lehman Road

- Punch list items addressed 12/1/2020
- Project closeout in progress

Burleson Street

- Based on pay estimates, overall project is 93% complete
- Items on punch list being addressed by contractor
- Finalization of work quantities in progress



Windy Hill Street & Drainage Project

- Construction began on November 30, 2020
- Richmond Branch structure walls, deck & north wings pour December 15th
- Windy Hill to open on or about December 22nd
- Phase 2 construction of south half of Windy Hill begins January 4, 2021





Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 71% complete
- One crew working on the Post Road lift station
- Second crew working on gravity and reclaimed water lines near TDCJ
- Third crew working on last bore on north end of project





WWTP Expansion Project

- Consent Agenda Item #13
 - For professional service agreement to design dewatering facility for inclusion into existing construction project
- Based on pay estimates, overall project is 27% complete
- Treatment pipe, form work, rebar and concrete placement continues on all major treatment units
- Continued installation of electrical duct banks and manholes throughout site
- No deviations between construction progress and construction schedule




WWTP Expansion Project (cont.)

November 27th Clarifiers 1A & 1B



December 12th Clarifiers 1A & 1B

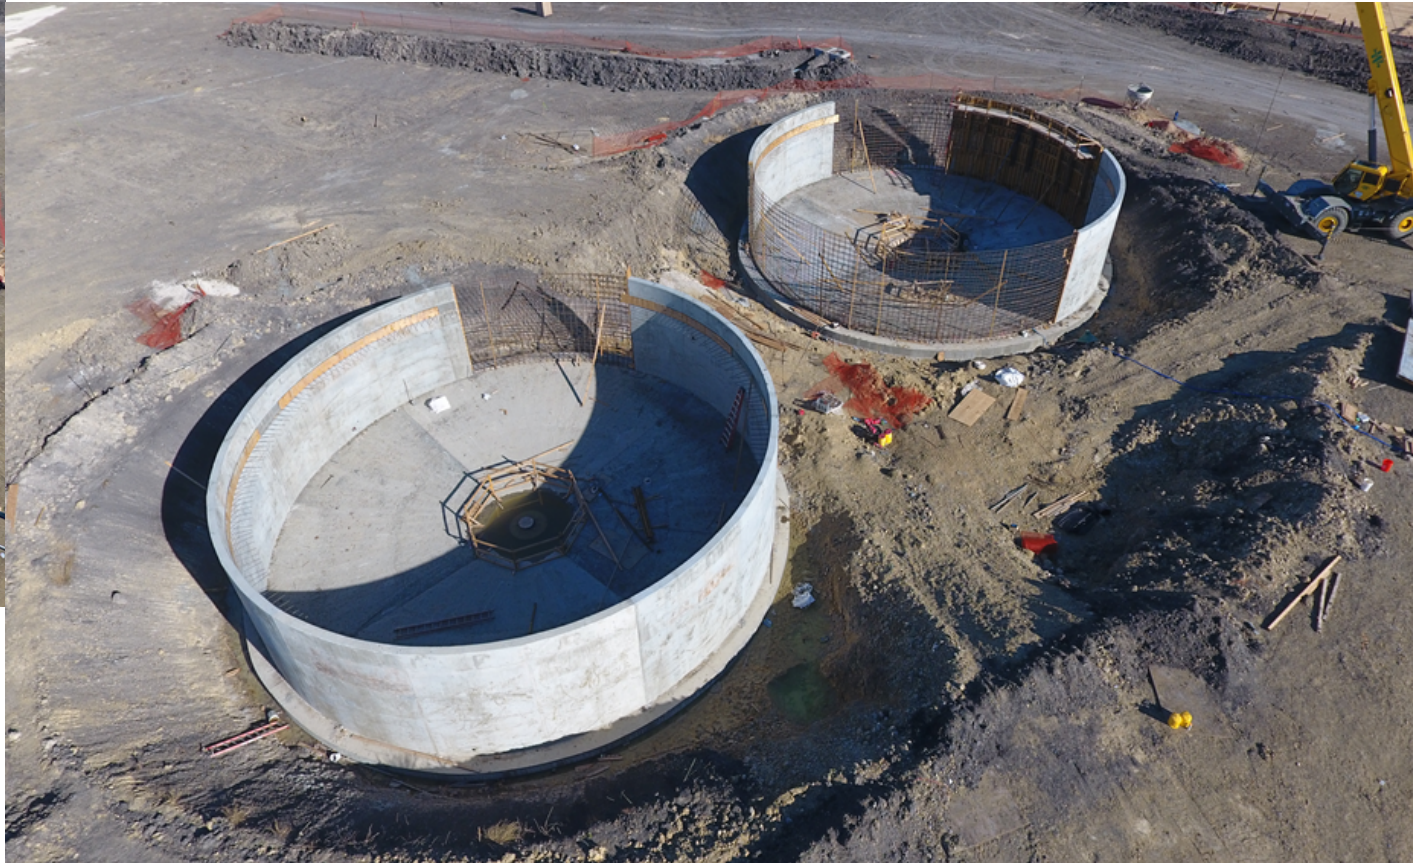



Bunton Creek Interceptor Ph 2

- Bunton Creek Village Lift Station to Wastewater Treatment Plant
- 250 calendar day contract
- Erosion control measures being installed





Well Site #4 Elevated Storage Tank Rehabilitation

- 150 calendar days for full completion
- Start date: January 1, 2021





Old Post Road

- Next meeting scheduled with Hays County on December 16, 2020 to continue project coordination
- TxDOT permitting underway
- Negotiations continuing for ROW
- Hays County reviewing draft interlocal agreement



Developer Project

Casetta Ranch Roundabout

- Construction started November 4, 2020
- Estimated duration 3 months
- Approximately 70% complete
- East/West movement open by the end of the year
- North connection will be closed to complete the construction tie-in on Goforth





Developer Project

Paramount Subdivision


- Opal Lane – traffic control plan has been approved
- Construction on Opal Lane could start this week but most likely construction will begin next week



Consent Agenda

SmartCovers

- Consent Agenda Item No. 12
 - Purchase of 3 SmartCovers primarily used to monitor Infiltration & Inflow of stormwater entering manholes

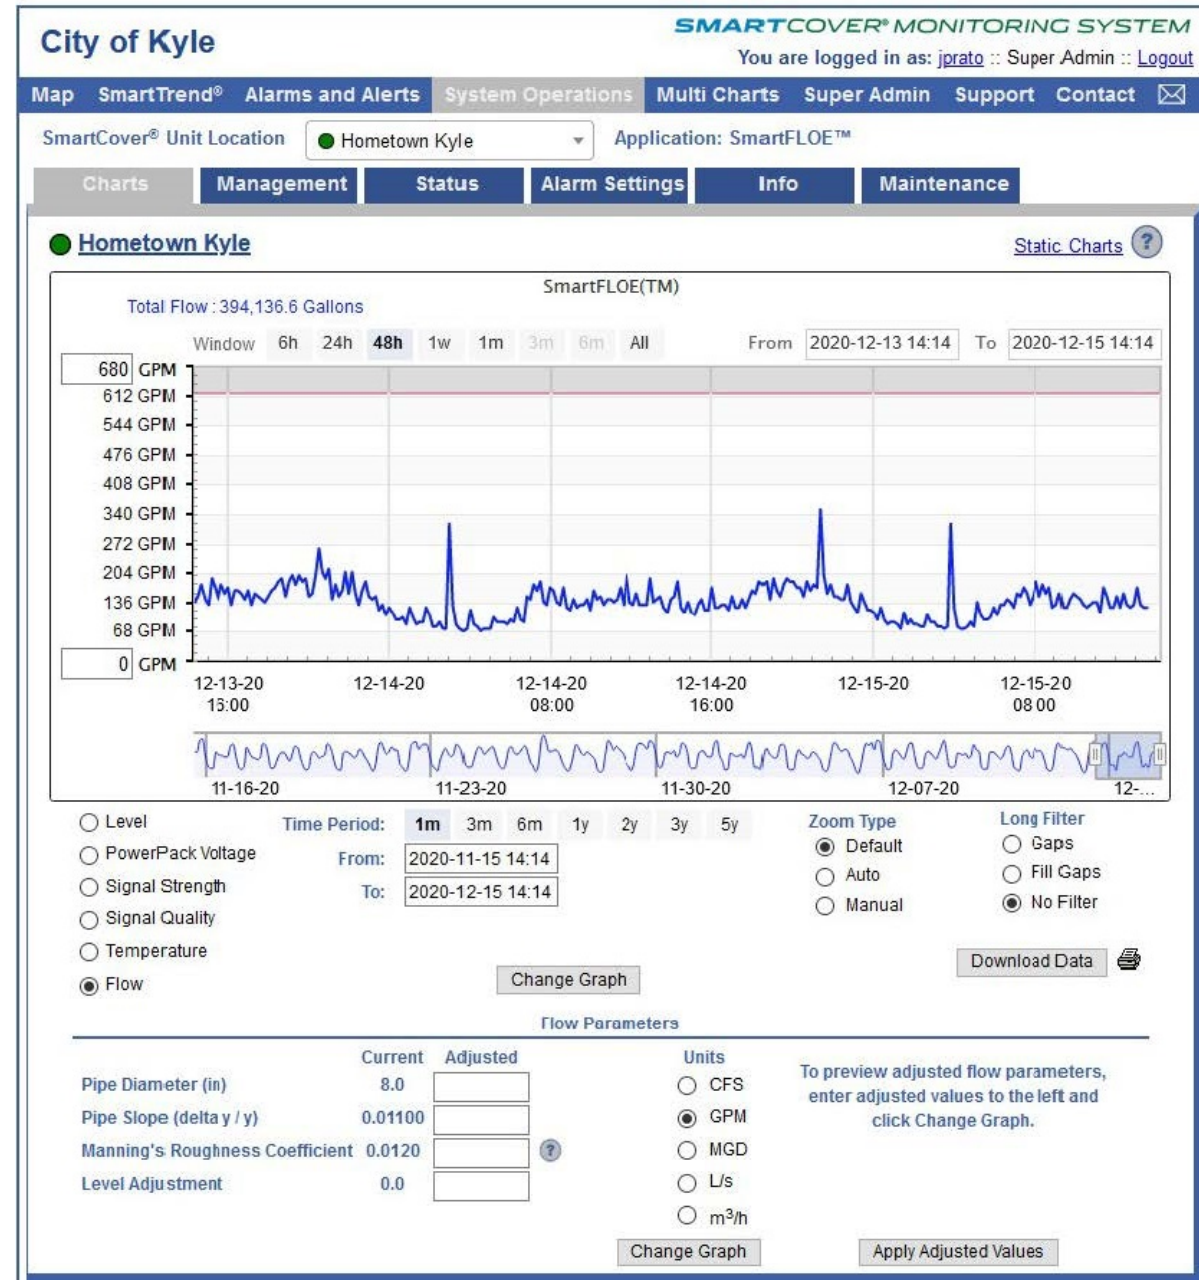



For info & updates on all projects visit:

cityofkyle.com/projects
