

CIP/Road Projects Update

December 17, 2019

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 46% complete
- Paved from Primrose to FM 150 but still closed for sidewalk & driveway crews
- <u>Tentative</u> opening of that section planned for later this month
- Overall project expected completion August 2020





Burleson Street


- Based on pay estimates, overall project is 66% complete
- Section from Center to Rodriguez is open to local traffic only
- Minimal work needed on retaining wall at the church (surface finish)
- Detention pond near completion
- Crews still working from Live Oak to south of James Adkins





Burleson Street (cont.)

- Rodriguez and Spring Branch remain closed
- Utility work continues from Rodriguez to James Adkins
- UPRR is currently onsite
- During the closure north of James Adkins, traffic will be allowed to use Burleson from Center to Star of Texas; however, workers will be finishing detailed work
- Estimated completion June 2020

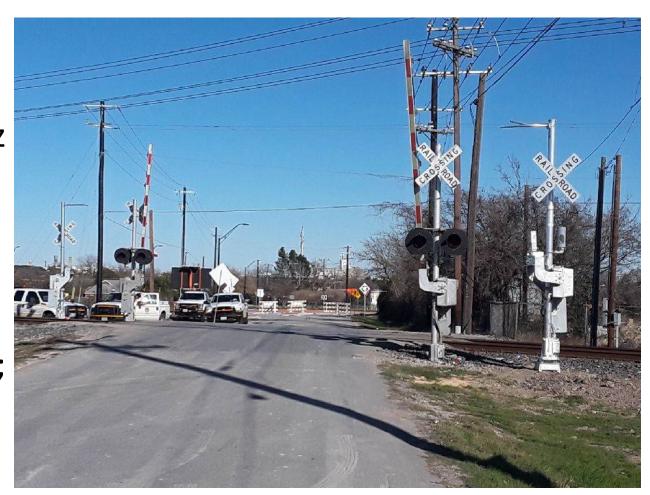



Kyle Crossing


- Project 98% complete
- Road open
- Punchlist items:
 - Signs (PW)
- Final walk-through to be scheduled





Bunton Creek Interceptor

- Overall Project is 96% complete
 - Still working on punchlist items
- Requesting a 2 month extension to request grand funding to pay portion of change order
 - The change order will be to provide erosion protection around new manhole
- 40% of Project is grant funded

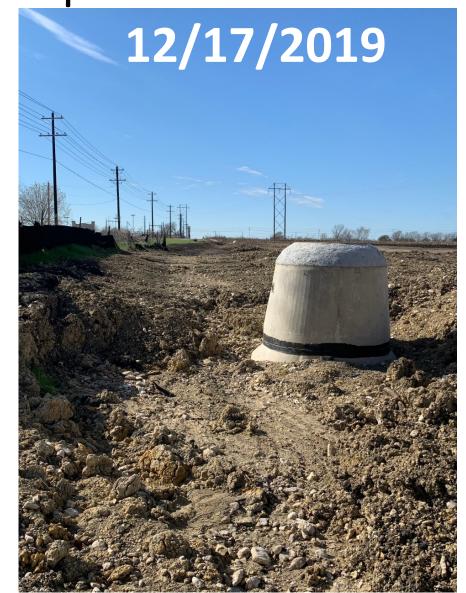



WWTP Expansion

- Bid opening December 3, 2019
 - 3 bids received
 - Bids will be vetted for apparent low bidder
 - Range of bids received \$28,893,400-\$30,921,000
- Postponed for January 21, 2020 City Council meeting in order to prepare funding plan





Other Projects

<u>Plum Creek Wastewater Interceptor Phase 1 Improvements (Springbranch)</u>

- Contractor estimates completion prior to Christmas holidays
 - Final walk-through scheduled for January
 - Construction entrance at Western Cove will be removed by contractor as part of punchlist

Marketplace Ave Extension (Streetlight)

Light is active





Consent Agenda

Windy Hill Road Improvements Project

- Consent Agenda Item #9
- Approve a professional services agreement with LJA ENGINEERING for design, and construction phase services
