



CIP/Road Projects Update

January 19, 2021

Leon Barba, P.E.

Engineering Department



Lehman Road

- Project closeout in progress

Burleson Street

- Based on pay estimates, overall project is 93% complete
- Items on punch list being addressed by contractor
- Finalization of work quantities in progress




Windy Hill Street & Drainage Project

- Project 16% complete
- Change Order No. 1 being executed
 - Allows 2-way traffic through construction area
 - 3.56% increase to contract
- Contractor working south half of Windy Hill Road (struct. & road)
- Side street intermittent closures (Indian Paintbrush & Cherrywood) begin Jan. 25 – Feb. 25, 2021 (weather permitting)



Windy Hill Street & Drainage Project (cont)

Phase 2 - South half of Windy Hill is constructed.
From Approximately 500 ft west of Cherrywood to Park St. Drive

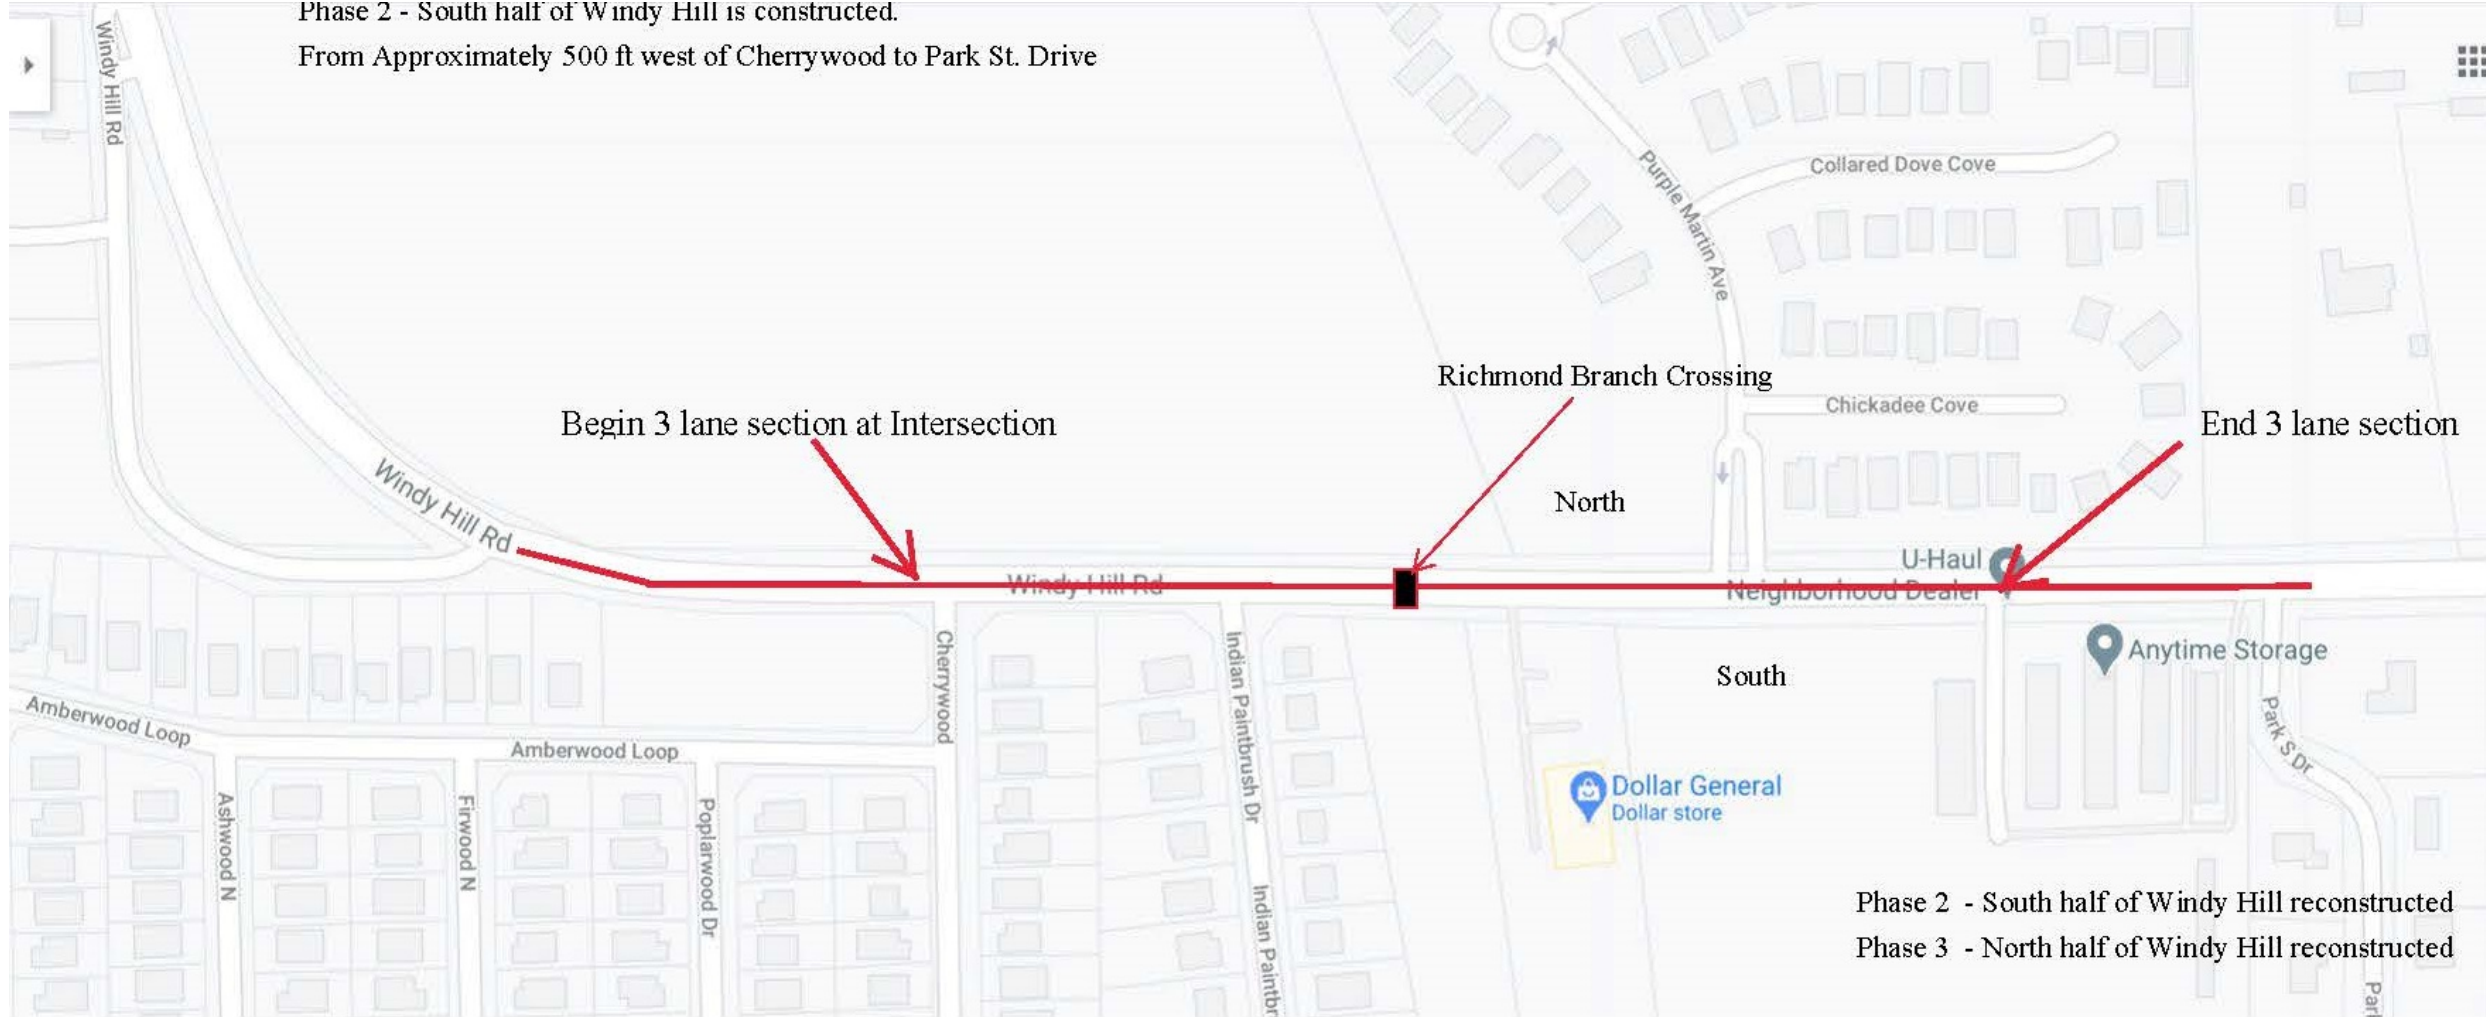

Phase 2 - South half of Windy Hill reconstructed
Phase 3 - North half of Windy Hill reconstructed



Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 73% complete
- Post Road lift station substantially complete
- Crew working on gravity and reclaimed water lines near TDCJ
- Reclaimed water line bore near completion





WWTP Expansion Project

- Based on pay estimates, overall project is 35% complete
- Treatment pipe, form work, rebar and concrete placement continues on all major treatment units
- Continued installation of electrical duct banks and manholes throughout site
- Additional crane onsite first week in January 2021
- No deviations between construction progress and construction schedule
- Expansion complete and on-line in March 2022

WWTP EXPANSION JANUARY 17, 2021

UV
Disinfection

Plant #1

Plant #2

Clarifiers

Digesters

Headworks &
Influent Lift Station

Aeration Basins

Aeration
Splitter Box

Operations
Building





Bunton Creek Interceptor Ph 2

- Erosion control measures installation completed
- Manholes & trenching are expected this week





Well Site #4 Elevated Storage Tank Rehabilitation

- Shrouding of tank this week
- Paint blasting, interior and exterior, to start next week





Old Post Road

- Next meeting scheduled with Hays County on February 3, 2021 to continue project coordination
- TxDOT permitting underway
- Negotiations continuing for ROW
- Hays County preparing interlocal agreement for the February 2, 2021 Council Meeting



Developer Project

Casetta Ranch Roundabout

- Construction started November 4, 2020
- Approximately 75% complete
- North connection closed except for southbound traffic
- Expected completion to be 6-8 weeks from today





Developer Project

Paramount Subdivision

- Opal Lane is closed due to construction at railroad crossing for quiet zone





For info & updates on all projects visit:

cityofkyle.com/projects
