



# CIP/Road Projects Update

January 5, 2021

Leon Barba, P.E.

Engineering Department



## **Lehman Road**

- Project closeout in progress

## **Burleson Street**

- Based on pay estimates, overall project is 93% complete
- Items on punch list being addressed by contractor
- Finalization of work quantities in progress



# Windy Hill Street & Drainage Project


- Project 16% complete
- Construction began on November 30, 2020
- Richmond Branch structure & upstream walls complete
- Windy Hill north half of road opened December 23<sup>rd</sup>
- Phase 2 construction underway





# Windy Hill Street & Drainage Project (cont)

Phase 2 - South half of Windy Hill is constructed from approximately 500 ft west of Cherrywood to Park S Drive

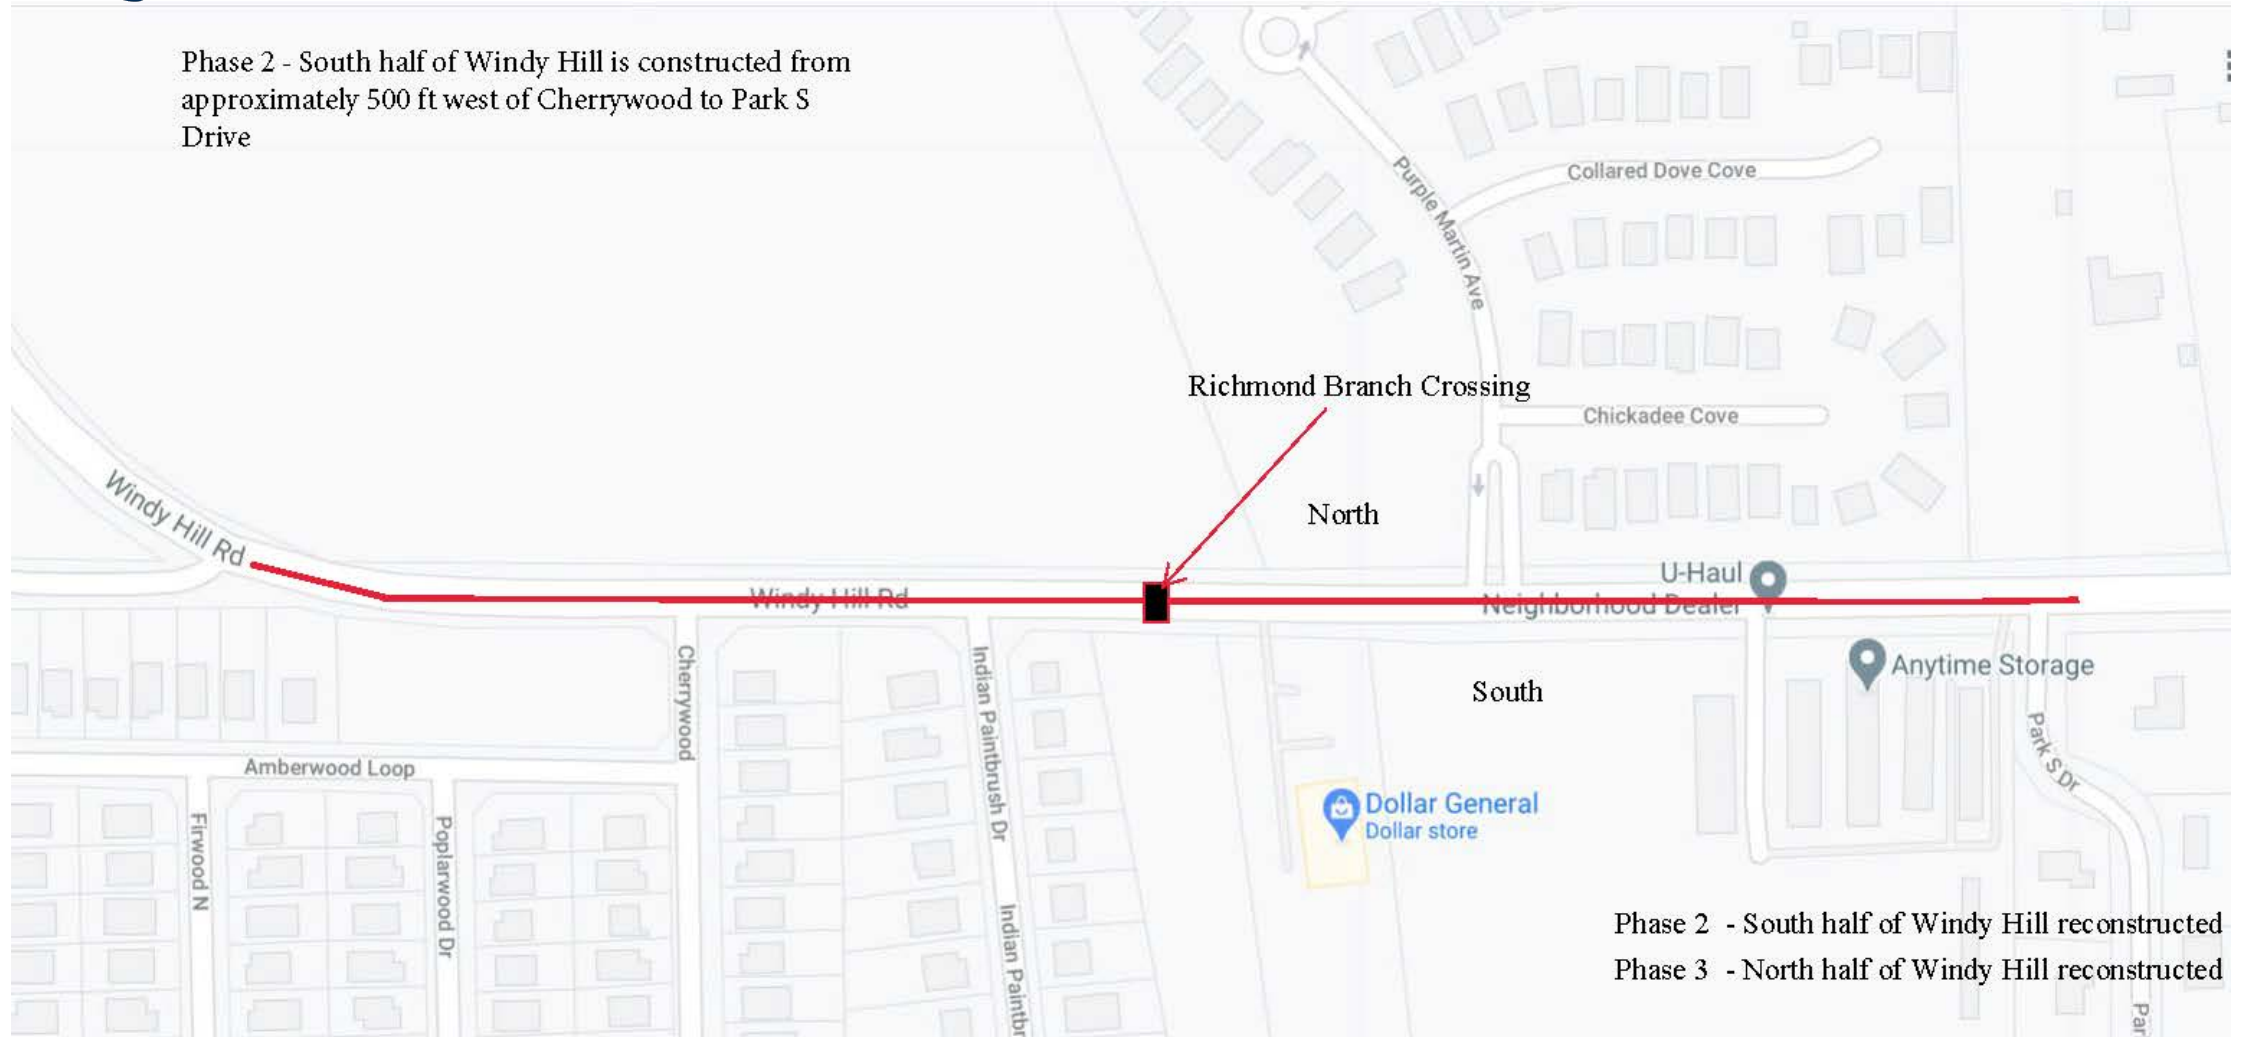

Phase 2 - South half of Windy Hill reconstructed  
Phase 3 - North half of Windy Hill reconstructed



# Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 71% complete
- Finishing the Post Road lift station
- Second crew working on gravity and reclaimed water lines near TDCJ
- Third crew working on last bore on north end of project





## WWTP Expansion Project

- Based on pay estimates, overall project is 27% complete with December pay application pending approval
- Treatment pipe, form work, rebar and concrete placement continues on all major treatment units
- Continued installation of electrical duct banks and manholes throughout site
- No deviations between construction progress and construction schedule

# WWTP EXPANSION DECEMBER 27, 2020

UV  
Disinfection

Digesters

Plant #1

Clarifiers

Headworks &  
Influent Lift Station

Plant #2

Aeration Basins

Aeration  
Splitter Box

Operations  
Building





# Bunton Creek Interceptor Ph 2

- Erosion control measures installation completed
- Manholes & trenching are expected next week



1/5/2021





# Well Site #4 Elevated Storage Tank Rehabilitation

- 150 calendar days for full completion
- Start date: January 4, 2021





## Old Post Road

- Next meeting scheduled with Hays County on January 13, 2021 to continue project coordination
- TxDOT permitting underway
- Negotiations continuing for ROW
- Hays County reviewing draft interlocal agreement
- Scheduled for Council approval in February



# Developer Project

## Casetta Ranch Roundabout

- Construction started November 4, 2020
- Estimated duration 3 months
- Approximately 70% complete
- East/West movement open
- North connection closed except for southbound traffic





# Developer Project

## Paramount Subdivision

- Construction on Opal Lane to start mid-next week with closure of Opal Lane



**For info & updates on all projects visit:**

**[cityofkyle.com/projects](http://cityofkyle.com/projects)**
