



CIP/Road Projects Update

October 6, 2020

Leon Barba, P.E.

Engineering Department



Lehman Road

- Based on pay estimates, overall project is 98% complete
- Contractor working on Final walk through items
- ADA inspection postponed to October 13, 2020
- Streetlights on
- Daily lane closure due to sidewalk repair north of Hallie





Burleson Street

- Based on pay estimates, overall project is 83% complete
- Items on preliminary punch list being addressed by contractor
- ADA inspection scheduled for October 12, 2020





Southside Wastewater Improvements Project

- Based on pay estimates, overall project is 64% complete
- One crew working on the Post Road lift station
- Second crew working on gravity and reclaimed water lines near Public Works
- Third crew working on 2nd bore at Post Road by IH-35





WWTP Expansion Project

- Based on pay estimates, overall project is 14.41% complete
- Aeration basin foundation slab complete
- Contractor requested to work on Saturdays to make up for lost time from rain events
- No impact to construction schedules critical path
- Installation of electrical duct banks and manholes ongoing



WWTP EXPANSION OCTOBER 2, 2020



Headworks

Plant #1

Plant #2

UV
Disinfection

Digesters

Clarifiers

Aeration
Basins

Aeration
Splitter Box

Electrical Manholes
& Duct Bank

Headworks Rebar Wall Installations





Upcoming Projects

Bunton Creek Interceptor Ph 2

- Consent Agenda Item #11
- Bunton Creek Village Lift Station to COK Wastewater Treatment Plant
- 250 calendar days
- Notice to Proceed: November 01, 2020
- Start Work Date: November 15, 2020
- Estimated cost - \$3.1M



Upcoming Projects

Kohlers Crossing Well Site #4 Elevated Storage Tank Rehabilitation

- Consent Agenda Item #13
- 150 calendar days for full completion
- Estimated start date: Mid-November 2020
- Estimated cost - \$350,000



Upcoming Projects

Elliott Branch Wastewater Improvements Phase 1

- Designed by RPS
- Bid Opening Date - October 21, 2020
- Estimated cost - \$6.2M

Windy Hill Street & Drainage Improvements

- Designed by LJA
- Scheduled for Council approval October 20, 2020
- Estimated cost - \$2.9M
- Construction to begin January 2021



Upcoming Projects

Old Post Road

- Designed by CP&Y
- Plans 100% complete
- TxDOT permitting underway; negotiations underway for ROW
- PW completed installation of waterline

Casetta Ranch Roundabout


- Developer project - construction of a roundabout at Bunton Lane & Goforth
- Construction to start late October 2020
- Estimated duration 3 months



Microsurfacing 2020

- Contractor mobilized October 5, 2020
- Estimated cost - \$500,000

MICROSURFACING WORK

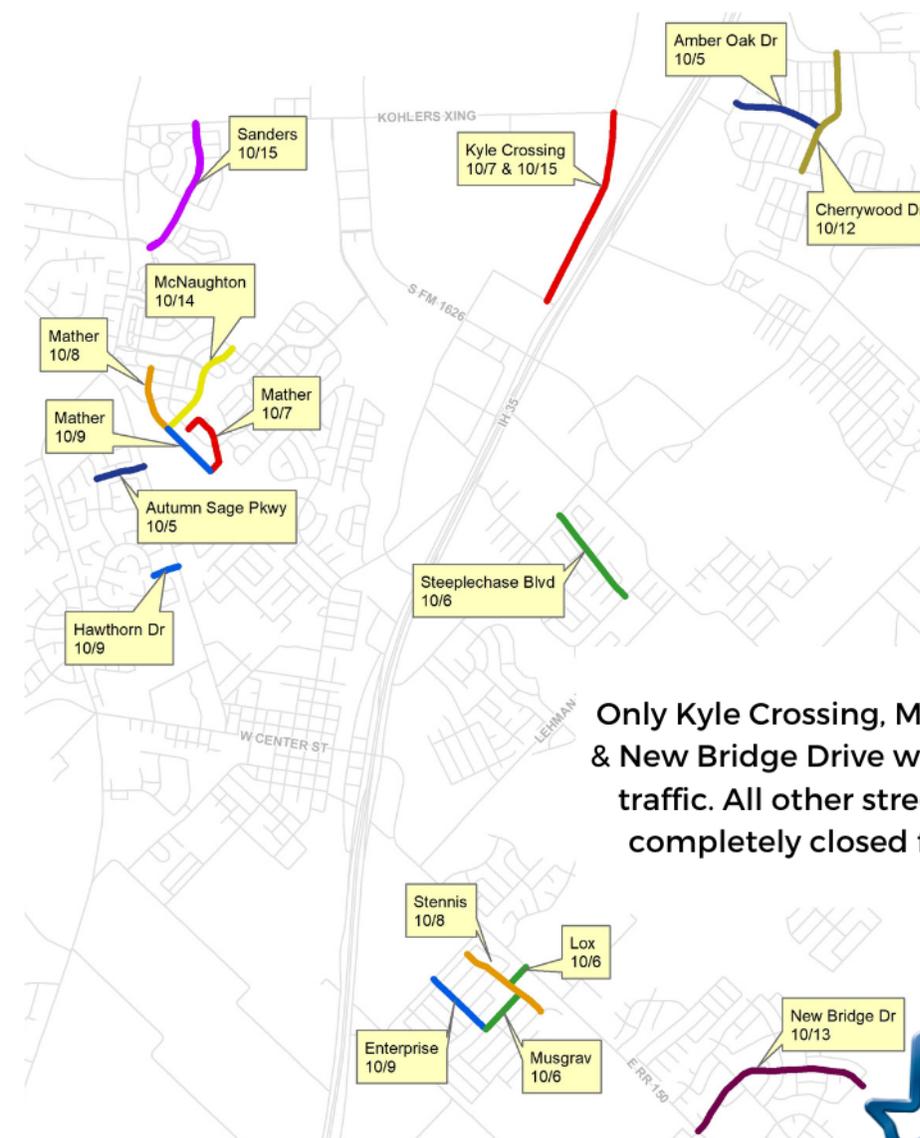

Only Kyle Crossing, McNaughton & New Bridge Drive will have thru traffic. All other streets will be completely closed for traffic.

CALL 512-262-1010 FOR MORE INFO

