Road Bond Project Timelines

Updated January 14, 2015

Task	Activity Description	% Comp.	Work Progress
A	Preliminary Engineering		
	Burleson	95	
	Bunton	95	
	Goforth	95	
	Lehman	100	
	Marketplace Ave	2	
B	Utility Engineering & Adjustments		
	Burleson	5	
	Bunton	45	
	Goforth	30	
	Lehman	50	
	Marketplace Ave	0	
C	Environmental Documentation & Approval		
	Burleson	0	
	Bunton	100	
	Goforth	70	
	Lehman	75	
	Marketplace Ave	0	
D	ROW Acquisition		
	Burleson	0	
	Bunton	0	
	Goforth	5	
	Lehman	5	
	Marketplace Ave	0	
E	Design (Plan Development)		
	Burleson	25	
	Bunton	75	
	Goforth	45	
	Lehman	30	
	Marketplace Ave	0	
F	Railroad Coordination		
	Burleson	5	
G	Advertising / Letting of Project /Awardance		
	Burleson	0	
	Bunton	0	
	Goforth	0	
	Lehman	0	
	Marketplace Ave	0	
H	Begin Construction		
	Burleson	0	
	Bunton	0	
	Goforth	0	
	Lehman	0	
	Marketplace Ave	0	

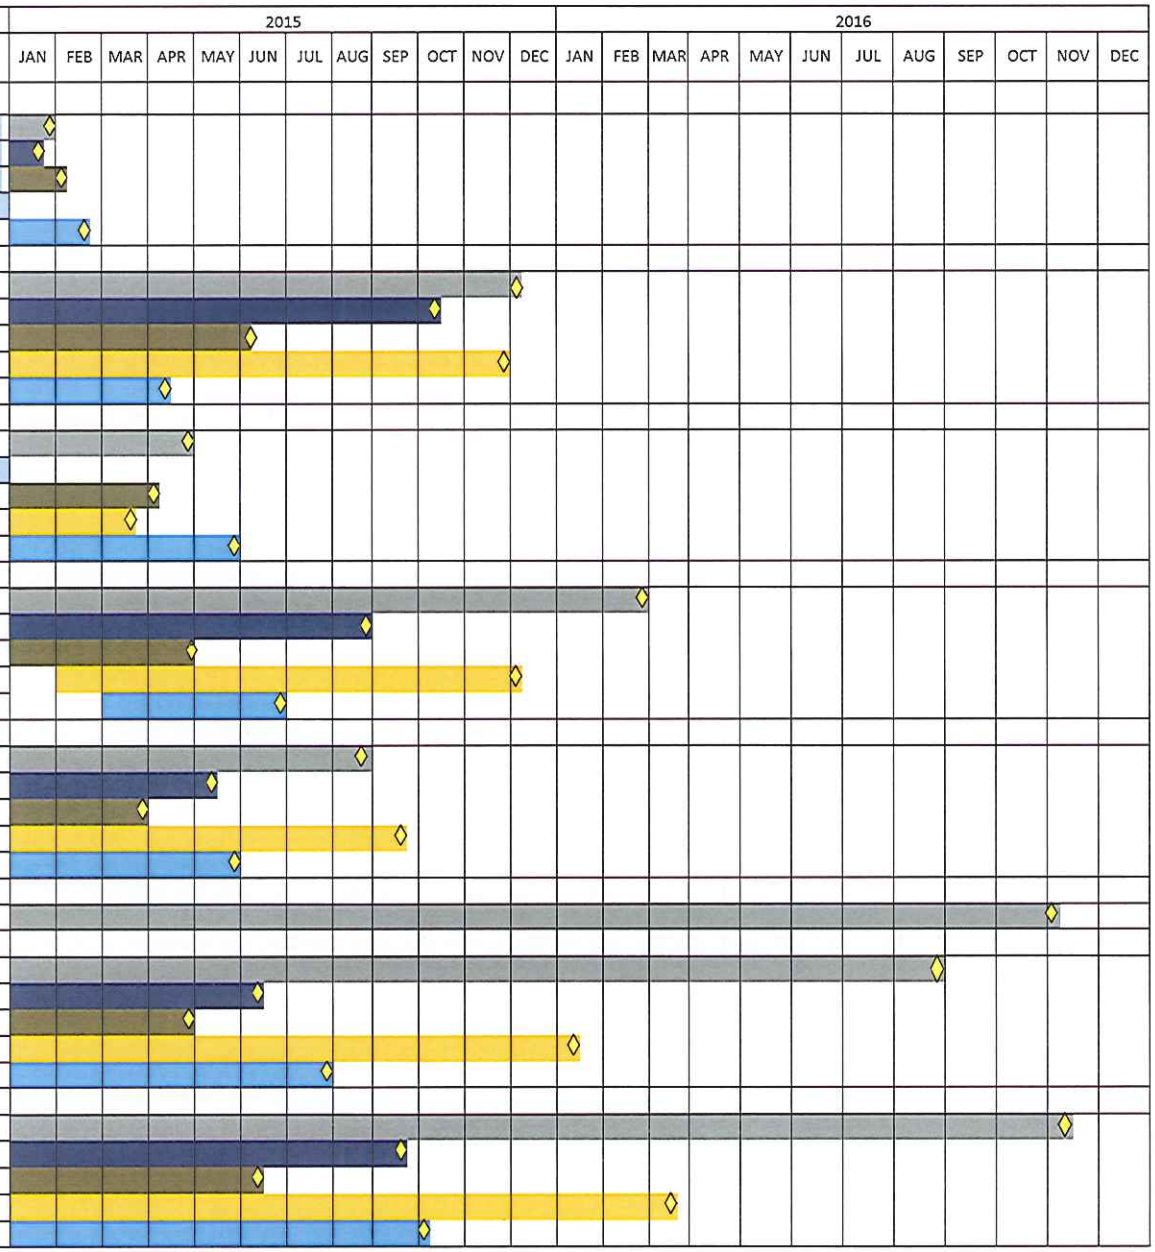

Project Milestone / Deliverable Date
Project On Schedule
Project Ahead of Schedule
Project Behind Schedule

Utility adjustment dates have not been certified by Utility Owners.
